


METALWORKS® ESTIMATE SHEET

JOB NAME _____ DATE _____

ADDRESS: _____ PHONE # _____

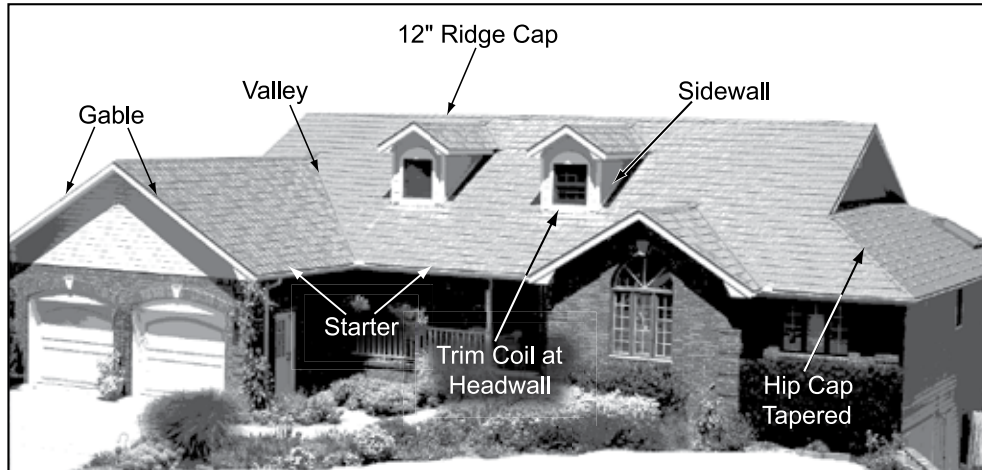

☐ **STONECREST® SLATE**

- ☐ Sequoia Red
- ☐ Vermont Blue
- ☐ Timber Brown
- ☐ Forest Green
- ☐ Sierra Slate Grey
- ☐ River Rock Brown
- ☐ Quaker Green
- ☐ Canyon Copper Bronze

☐ **STONECREST® TILE**

- ☐ Vermont Blue
- ☐ Sierra Slate Grey
- ☐ Quaker Green

☐ **ASTONWOOD®**

- ☐ Sequoia Red
- ☐ Vermont Blue
- ☐ Timber Brown
- ☐ Forest Green
- ☐ Sierra Slate Grey
- ☐ River Rock Brown
- ☐ Quaker Green
- ☐ Canyon Copper Bronze

SHINGLES

Roof Areas Measured in Feet:

_____	X	=	_____	sqft
_____	X	=	_____	sqft
_____	X	=	_____	sqft
_____	X	=	_____	sqft
_____	X	=	_____	sqft
_____	X	=	_____	sqft
_____	X	=	_____	sqft
TOTAL ROOF AREA =				_____ sqft

TRIM COMPONENTS

Starter	_____ ft	Ridge	_____ ft
Gable	_____ ft	Hip	_____ ft
Headwall	_____ ft	Sidewall	_____ ft
Valley	_____ ft	J Channel	_____ ft

TOTAL SHINGLE CARTONS

AstonWood	_____ sqft div by	50 =	_____ total ctns
StoneCrest Slate	_____ sqft div by	50 =	_____ total ctns
StoneCrest Tile	_____ sqft div by	50 =	_____ total ctns

SHINGLE COST

Total Shingle ctns _____ X \$ _____ per ctn = \$ _____

(Figure your waste factor for all calculations)


*METAL ACCESSORIES

STARTER/ EAVE

10 pcs/ctn 10 ft. length

Eave Edge

Total Eave Length _____ ÷ 10ft = _____ pcs X \$ _____ per pc = \$ _____ cost




GABLE/ RAKE

10 pcs/ctn 10 ft. length

Rake Edge

Total Gable Length _____ ÷ 10ft = _____ pcs X \$ _____ per pc = \$ _____ cost




12 INCH HIP & RIDGE CAP

25 pcs/ctn 25 lineal ft.

Ridge Cap

Total Ridge Length _____ ÷ 25ft = _____ ctns X \$ _____ per ctn = \$ _____ cost



HIP CAP TAPERED


50 pcs/ctn 50 lineal ft.

AstonWood Hip Cap

Total Ridge Length _____ ÷ 50ft = _____ ctns X \$ _____ per ctn = \$ _____ cost

StoneCrest Hip Cap

Total Ridge Length _____ ÷ 50ft = _____ ctns X \$ _____ per ctn = \$ _____ cost



TRIM COIL

22-1/4" X 50'

_____ ctns \$ _____ cost



SIDEWALL

5 pcs/ctn 10 ft. length


Total Sidewall Length _____ ÷ 10ft = _____ pcs X \$ _____ per pc = \$ _____ cost



VALLEY

5 pcs/ctn 10 ft. length


Total Valley Length _____ ÷ 10ft = _____ pcs X \$ _____ per pc = \$ _____ cost



J CHANNEL

10 pcs/ctn 10 ft. length

Total J Channel Length _____ ÷ 10ft = _____ pcs X \$ _____ per pc = \$ _____ cost



CLIPS

400 clips per ctn (+/- 100 clips per square)

_____ ctns X \$ _____ per ctn = \$ _____ cost



SCREWS

50 screws per bag


_____ bags X \$ _____ per bag = \$ _____ cost



SNOW GUARDS

100 snow guards/ctn

_____ ctns X \$ _____ per ctn = \$ _____ cost



*Visit tamko.com and view application instructions to determine what accessories are needed.

NON-METAL ACCESSORIES

HIP & RIDGE SEAL

4" X 50'

_____ rolls X \$ _____ per roll = \$ _____ cost



TOUCH-UP PAINT

2 oz. bottle

_____ btls X \$ _____ per btl = \$ _____ cost



TAMKO UNDERLAYMENTS

TW METAL AND TILE UNDERLAYMENT

ROLL CONTAINS

2 sq. roll

ROLL COVERAGE**

1.79 sq. _____ rolls X \$ _____ roll = \$ _____ cost

TW UNDERLAYMENT

2 sq. roll

1.79 sq. _____ rolls X \$ _____ roll = \$ _____ cost

TAMKO NO. 30 FELT

2.16 sq. roll

2.04 sq. _____ rolls X \$ _____ roll = \$ _____ cost

SUPERX® 30 UNDERLAYMENT

2.16 sq. roll

2.04 sq. _____ rolls X \$ _____ roll = \$ _____ cost

SYNTHETIC GUARD PLUS UNDERLAYMENT

10.04 sq. roll

9.21 sq. _____ rolls X \$ _____ roll = \$ _____ cost

VENTILATION

RAPID RIDGE® VENTILATION

☐ 20 ft. roll ☐ 50 ft. roll 1.79 sq. _____ rolls X \$ _____ roll = \$ _____ cost

TOTAL TAMKO MATERIAL COST \$ _____

NOTE: THIS SHEET IS PROVIDED BY TAMKO FOR CONVENIENCE PURPOSES ONLY AND THE USER IS SOLELY RESPONSIBLE FOR ALL CALCULATIONS AND ESTIMATES ASSOCIATED WITH THE USE HEREOF. TAMKO EXPRESSLY DISCLAIMS ANY AND ALL LIABILITIES ASSOCIATED WITH THE USE OF THIS SHEET OR THE INFORMATION PROVIDED HEREIN. Information included in this sheet was accurate at the time of printing. To obtain a copy of the most current version of this brochure, visit us online at www.tamko.com or call us at 1-800-641-4691. ©2017 TAMKO Building Products, Inc. TAMKO, MetalWorks, StoneCrest and AstonWood are registered trademarks of TAMKO Building Products, Inc. Rapid Ridge is a registered trademark of Benjamin Obdyke.
