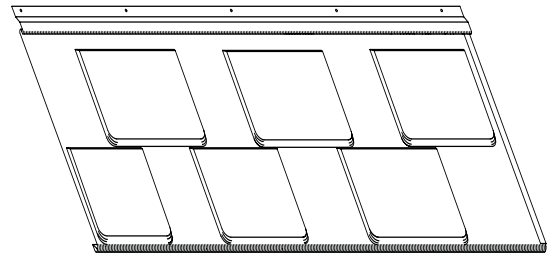# Advanta Estimating Sheet

Standard _____

Americana _____

Panels

Roof Areas :

_____ x _____ = _____ sqft

_____ x _____ = _____ sqft

_____ x _____ = _____ sqft

_____ x _____ = _____ sqft

_____ x _____ = _____ sqft

_____ x _____ = _____ sqft

_____ x _____ = _____ sqft

Total Roof Area = _____ sqft

Trim Components

Eave	_____	**Ridge**	_____
Gable	_____	**Hip**	_____
Headwall	_____	**Sidewall**	_____
Valley	_____	**Shed Ridge**	_____

Enter total footage required for each condition listed above

- -

Panel Square Footage   HAS300

Total Roof Area x 1.10 = _____ sqft

Total Cartons   Panel Square Footage div. by 50

_____ cartons (round to nearest full carton)

Eave

HSA114 Drip edge   Eave div. by 9.5   = _____ pcs @ 10'-0"

Gable

HSA114 Drip Edge   Gable div. by 9.5 = _____ pcs @ 10'-0"

HSA201 Channel Trim   Same qty as cap = _____ pcs @ 10'-0"

Ridge

HSA303 Rolled Ridge/Hip cap   Ridge div. by 9.5 = _____ pcs @ 10'-0"

Hip

HSA303 Rolled Ridge/Hip cap   Ridge div. by 9.5 = _____ pcs @ 10'-0"

Headwall

HSA500 Headwall   Headwall div. by 9.5 = _____ pcs @ 10'-0"

Sidewall

HSA411 Sidewall   Sidewall div. by 9.5 = _____ pcs @ 10'-0"

HSA440 Step Flashing   Sidewall x 1 = _____ pcs @ 14"

Valley

HSA801 Valley   Valley div. by 9.5 = _____ pcs @10'-0"

HSA805 Valley Cover   Same qty as Valley = _____ pcs @ 10'-0"

Shed Ridge

HSA342 Shed Ridge   Shed Ridge div. by 9.5 = _____ pcs @10'-0"

Accessories _____

HVC903 Valley Clips   HSA801 Valley x 12 = _____ pcs (round to nearest 50)

_____

** RSS213 1 1/2" Wafer Head Screws   Total Cartons x 150 = _____ pcs (round to nearest 100)

OR

** SWR402 2" Ring Shank Grommetted Nails   Total Cartons x 150 = _____ pcs (round to nearest 100)

_____

RSR3xx Rivets   Total Roof Area div. by 15 = _____ pcs (round to nearest 50)

SWR9XX 2" Ptd Gasketed Screw   (HSA303 Rolled Ridge/Hip x 12) + (HSA500 Headwall x 6) +
        (HSA342 Shed Ridge x 12) =   _____ pcs   (round to nearest 100)

SWR8XX 7/8"Ptd Gasketed Stitch Screw HSA805 Valley Cover x 6 = _____ pcs (round to nearest 50)

RSC312 Butyl Tape 50'   HSA201 Channel Trim + HSA805 Valley Cover div. by 4.5 = _____ rolls

RSC350 Expandable Sealant Tape   ((HSA303 Rolled Ridge/Hip x 2) + HSA500 Headwall +
        HSA342 Shed Ridge) div. total by 1.75 = _____ pcs

SCR800 Closure Tape HSA303 Rolled Ridge/Hip div. by 4.5   = _____ *rolls*

RST2XX Touch up Paint 2 oz. _____ ea
